

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	Resource Names	Oct 4, '20													
								T	F	S	S	M	T	W	T	F	S	S	M		
1		Mobilization	1 day	Mon 11/9/20	Mon 11/9/20																
2		Erosion Control	1 day	Mon 11/9/20	Mon 11/9/20																
3		Traffic Control Set Up	1 day	Tue 11/10/20	Tue 11/10/20																
4		Sawcutting	4 days	Wed 11/11/20	Mon 11/16/20																
5		Demo Surfacing and Existing Mahnoles	30 days	Thu 11/12/20	Wed 12/23/20																
6		Sewer Mainline and Manhole Install	30 days	Thu 11/12/20	Wed 12/23/20																
7		Storm Manhole Install	10 days	Thu 11/12/20	Wed 11/25/20																
8		Sewer Lateral Install	30 days	Thu 11/12/20	Wed 12/23/20																
9		Testing of Mainline, Laterals, and Maholes	30 days	Thu 11/12/20	Wed 12/23/20																
10		Bypass Pumping	30 days	Thu 11/12/20	Wed 12/23/20																
11		Concrete Curb Install	2 days	Mon 12/28/20	Tue 12/29/20																
12		Concrete Surfacing Install	4 days	Wed 12/30/20	Mon 1/4/21																
13		Asphalt Paving	2 days	Tue 1/5/21	Wed 1/6/21																
14		Site Restoration	2 days	Thu 1/7/21	Fri 1/8/21																
15		Site Cleanup	1 day	Mon 1/11/21	Mon 1/11/21																


Project: Canby - S Ivy St Sanitar  
Date: Fri 10/2/20

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	Resource Names	Oct 4, '20							Oct 11			
								T	F	S	S	M	T	W	T	F	S	S
16		Demobilize/Close Out	1 day	Tue 1/12/21	Tue 1/12/21													

Project: Canby - S Ivy St Sanitar  
Date: Fri 10/2/20

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

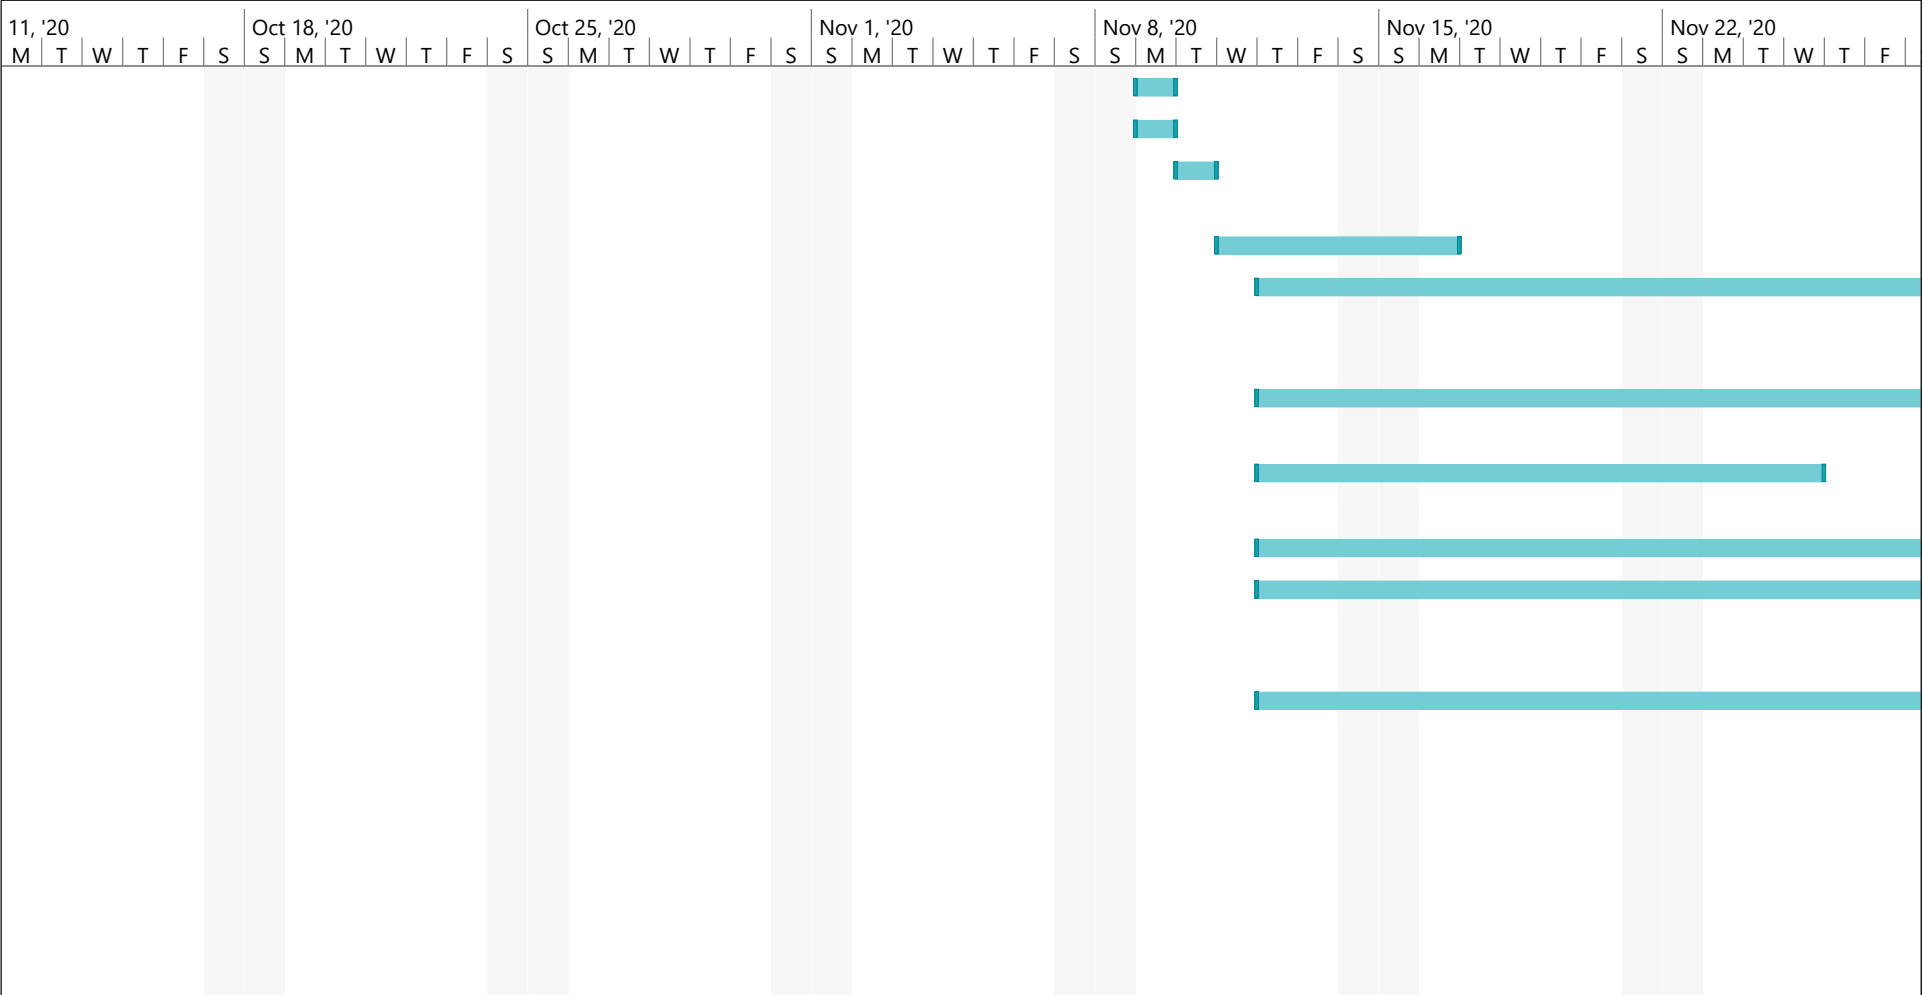

Project: Canby - S Ivy St Sanitar  
Date: Fri 10/2/20


Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

11, '20					Oct 18, '20					Oct 25, '20					Nov 1, '20					Nov 8, '20					Nov 15, '20					Nov 22, '20										
M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S




Project: Canby - S Ivy St Sanitar  
Date: Fri 10/2/20

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

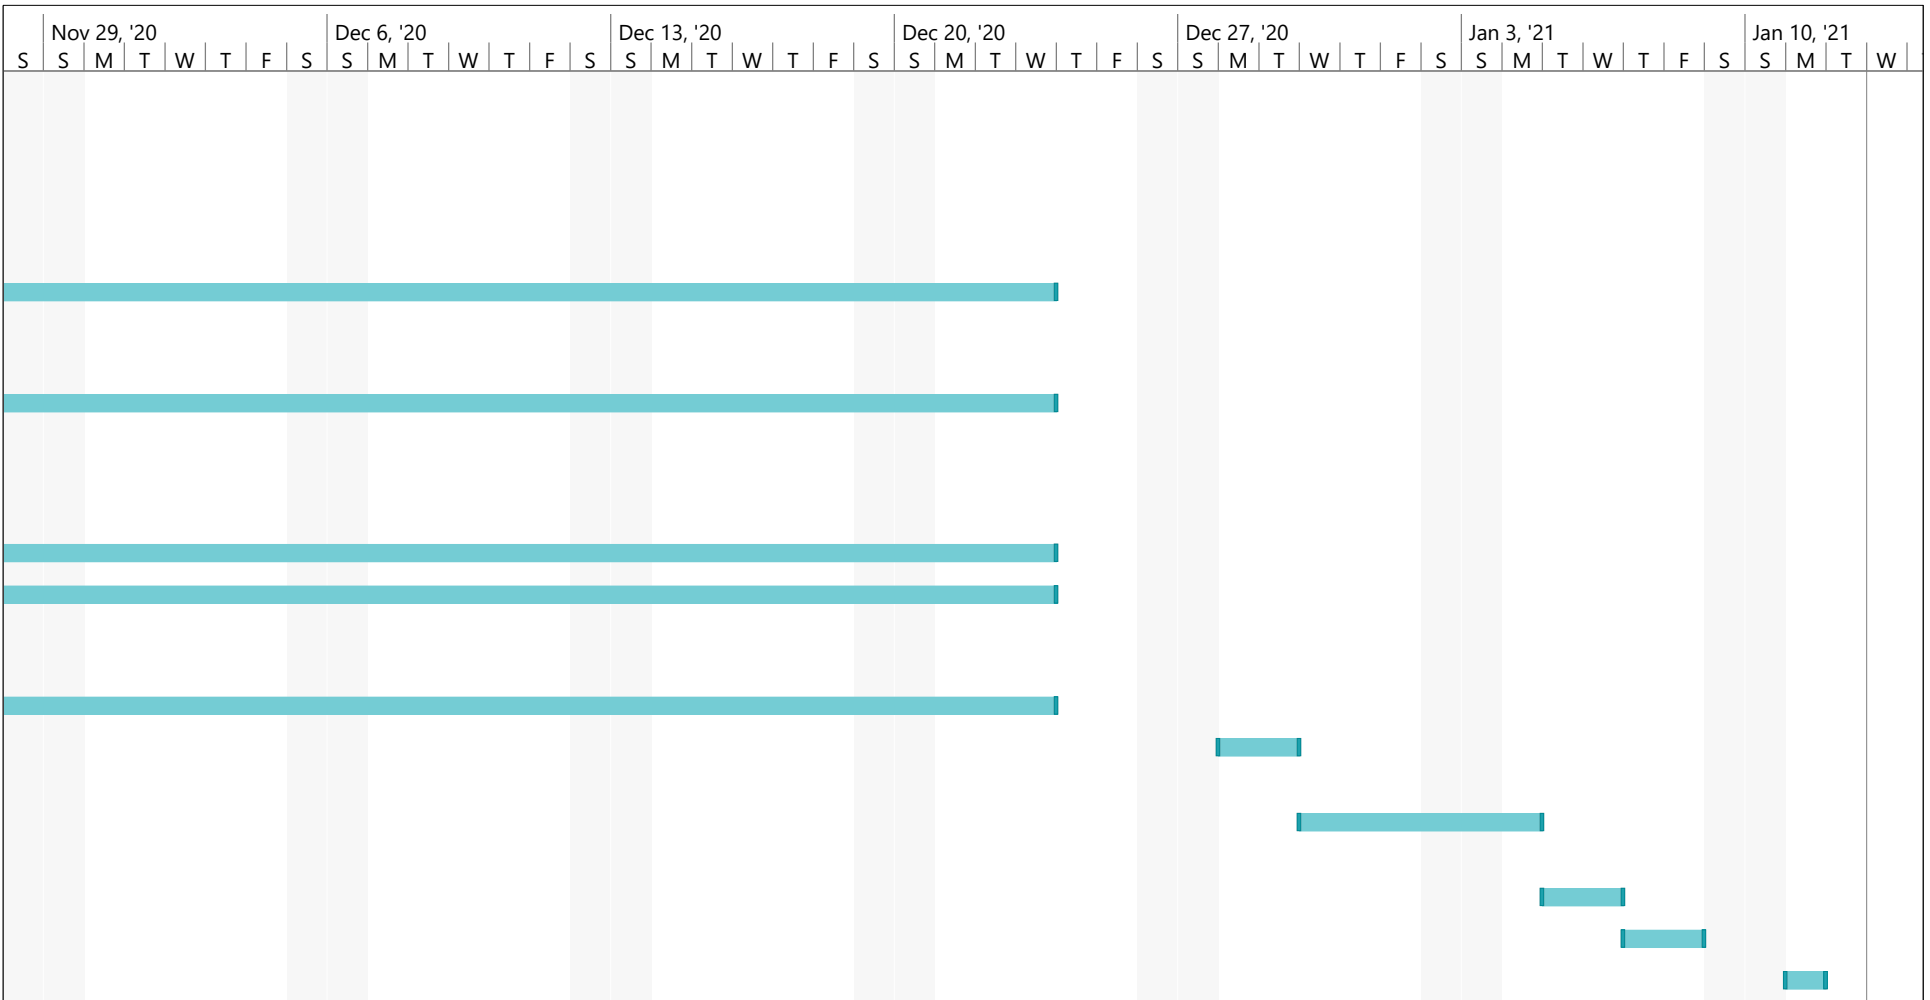

Project: Canby - S Ivy St Sanitar  
Date: Fri 10/2/20

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			



Project: Canby - S Ivy St Sanitar  
Date: Fri 10/2/20

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			
